
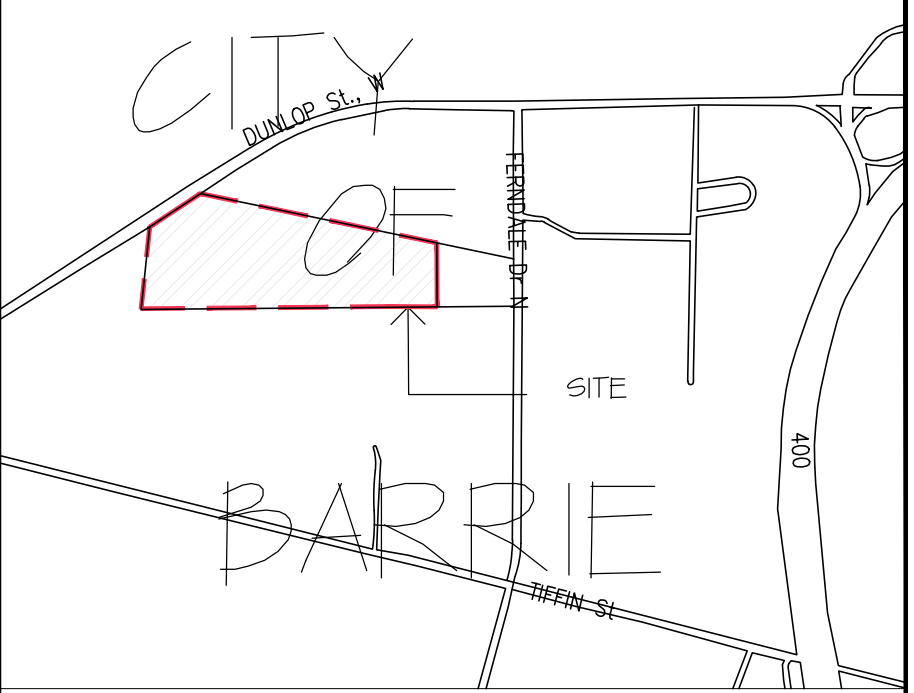


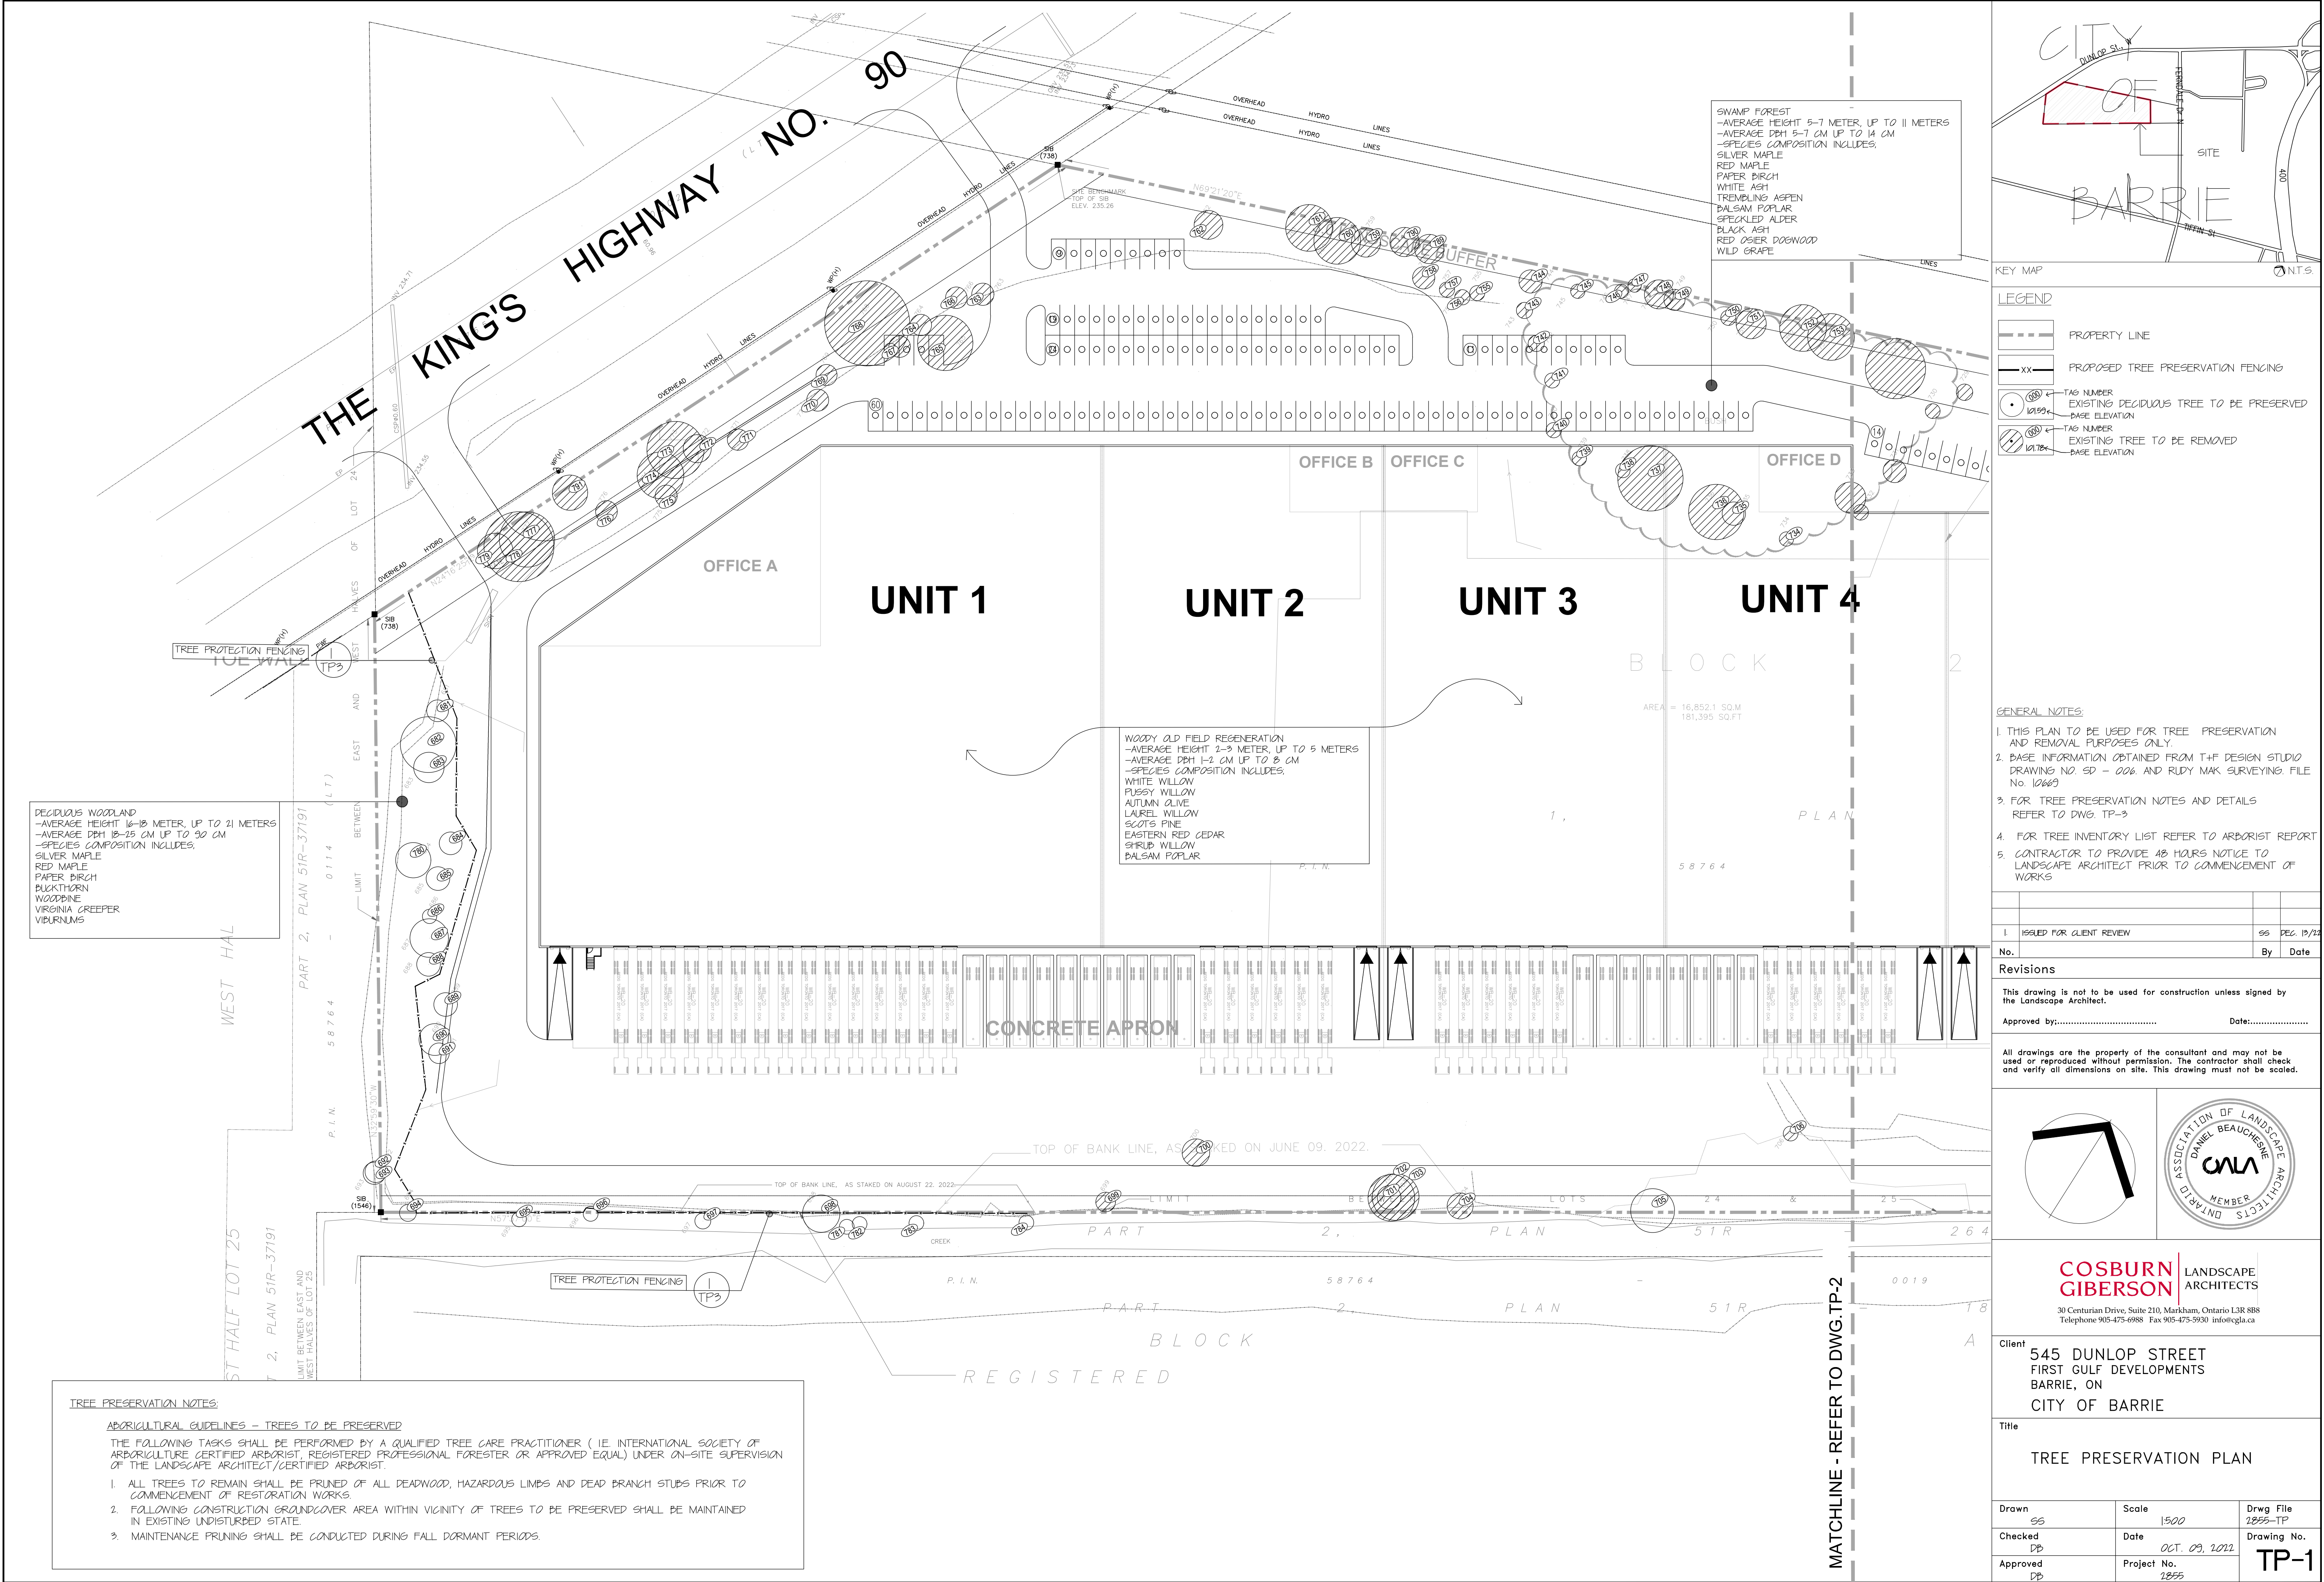

LEGEND

	PROPERTY LINE
	PROPOSED TREE PRESERVATION FENCING
	TAG NUMBER
	EXISTING DECIDUOUS TREE TO BE PRESERVED
	EXISTING TREE TO BE REMOVED

GENERAL NOTES:

- THIS PLAN TO BE USED FOR TREE PRESERVATION AND REMOVAL PURPOSES ONLY.
- BASE INFORMATION OBTAINED FROM T+H DESIGN STUDIO DRAWING NO. SD - 006 AND RUDY MAK SURVEYING FILE NO. 10669
- FOR TREE PRESERVATION NOTES AND DETAILS REFER TO DWG. TP-3
- FOR TREE INVENTORY LIST REFER TO ARBORIST REPORT
- CONTRACTOR TO PROVIDE 48 HOURS NOTICE TO LANDSCAPE ARCHITECT PRIOR TO COMMENCEMENT OF WORKS


1	ISSUED FOR CLIENT REVIEW	SS	DEC 19/22
No.		By	Date

Revisions

This drawing is not to be used for construction unless signed by the Landscape Architect.

Approved by:..... Date:.....

All drawings are the property of the consultant and may not be used or reproduced without permission. The contractor shall check and verify all dimensions on site. This drawing must not be scaled.

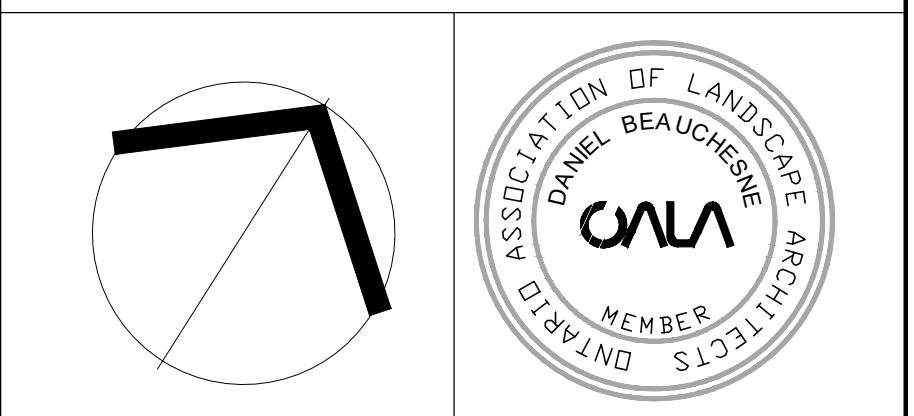

COSBURN GIBSON LANDSCAPE ARCHITECTS
30 Centurian Drive, Suite 210, Markham, Ontario L3R 8B8
Telephone 905-475-6988 Fax 905-475-5930 info@cgl.ca

Client
**545 DUNLOP STREET
FIRST GULF DEVELOPMENTS
BARRIE, ON
CITY OF BARRIE**

Title
TREE PRESERVATION PLAN



Drawn SS	Scale 1:500	Drwg File 2855-TP
Checked DB	Date OCT. 03, 2022	Drawing No.
Approved DB	Project No. 2855	TP-1

DECIDUOUS WOODLAND
-AVERAGE HEIGHT 16-18 METER, UP TO 21 METERS
-AVERAGE DBH 18-25 CM UP TO 30 CM
-SPECIES COMPOSITION INCLUDES:
SILVER MAPLE
RED MAPLE
PAPER BIRCH
BUCKTHORN
WOODPINE
VIRGINIA CREEPER
VIBURNUMS

WOODY OLD FIELD REGENERATION
-AVERAGE HEIGHT 2-3 METER, UP TO 5 METERS
-AVERAGE DBH 1-2 CM UP TO 8 CM
-SPECIES COMPOSITION INCLUDES:
WHITE WILLOW
PUSSY WILLOW
AUTUMN OLIVE
LAUREL WILLOW
SCOTS PINE
EASTERN RED CEDAR
SHRUB WILLOW
BALSAM POPLAR

SWAMP FOREST
-AVERAGE HEIGHT 5-7 METER, UP TO 11 METERS
-AVERAGE DBH 5-7 CM UP TO 14 CM
-SPECIES COMPOSITION INCLUDES:
SILVER MAPLE
RED MAPLE
PAPER BIRCH
WHITE ASH
TREMBLING ASPEN
BALSAM POPLAR
SPECKLED ALDER
BLACK ASH
RED OILER DOGWOOD
WILD GRAPE

- TREE PRESERVATION NOTES:
- ARBORICULTURAL GUIDELINES - TREES TO BE PRESERVED
- THE FOLLOWING TASKS SHALL BE PERFORMED BY A QUALIFIED TREE CARE PRACTITIONER (IE INTERNATIONAL SOCIETY OF ARBORICULTURE CERTIFIED ARBORIST, REGISTERED PROFESSIONAL FORESTER OR APPROVED EQUAL) UNDER ON-SITE SUPERVISION OF THE LANDSCAPE ARCHITECT/CERTIFIED ARBORIST.
- ALL TREES TO REMAIN SHALL BE PRUNED OF ALL DEADWOOD, HAZARDOUS LIMBS AND DEAD BRANCH STUBS PRIOR TO COMMENCEMENT OF RESTORATION WORKS.
 - FOLLOWING CONSTRUCTION GROUNDCOVER AREA WITHIN VICINITY OF TREES TO BE PRESERVED SHALL BE MAINTAINED IN EXISTING UNDISTURBED STATE.
 - MAINTENANCE PRUNING SHALL BE CONDUCTED DURING FALL DORMANT PERIODS.

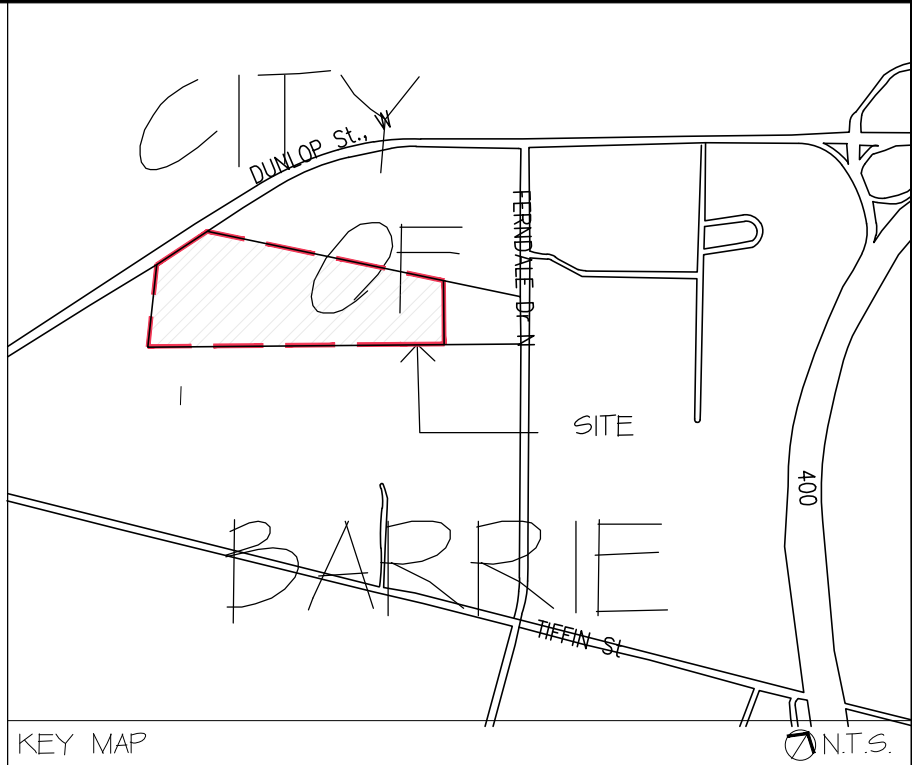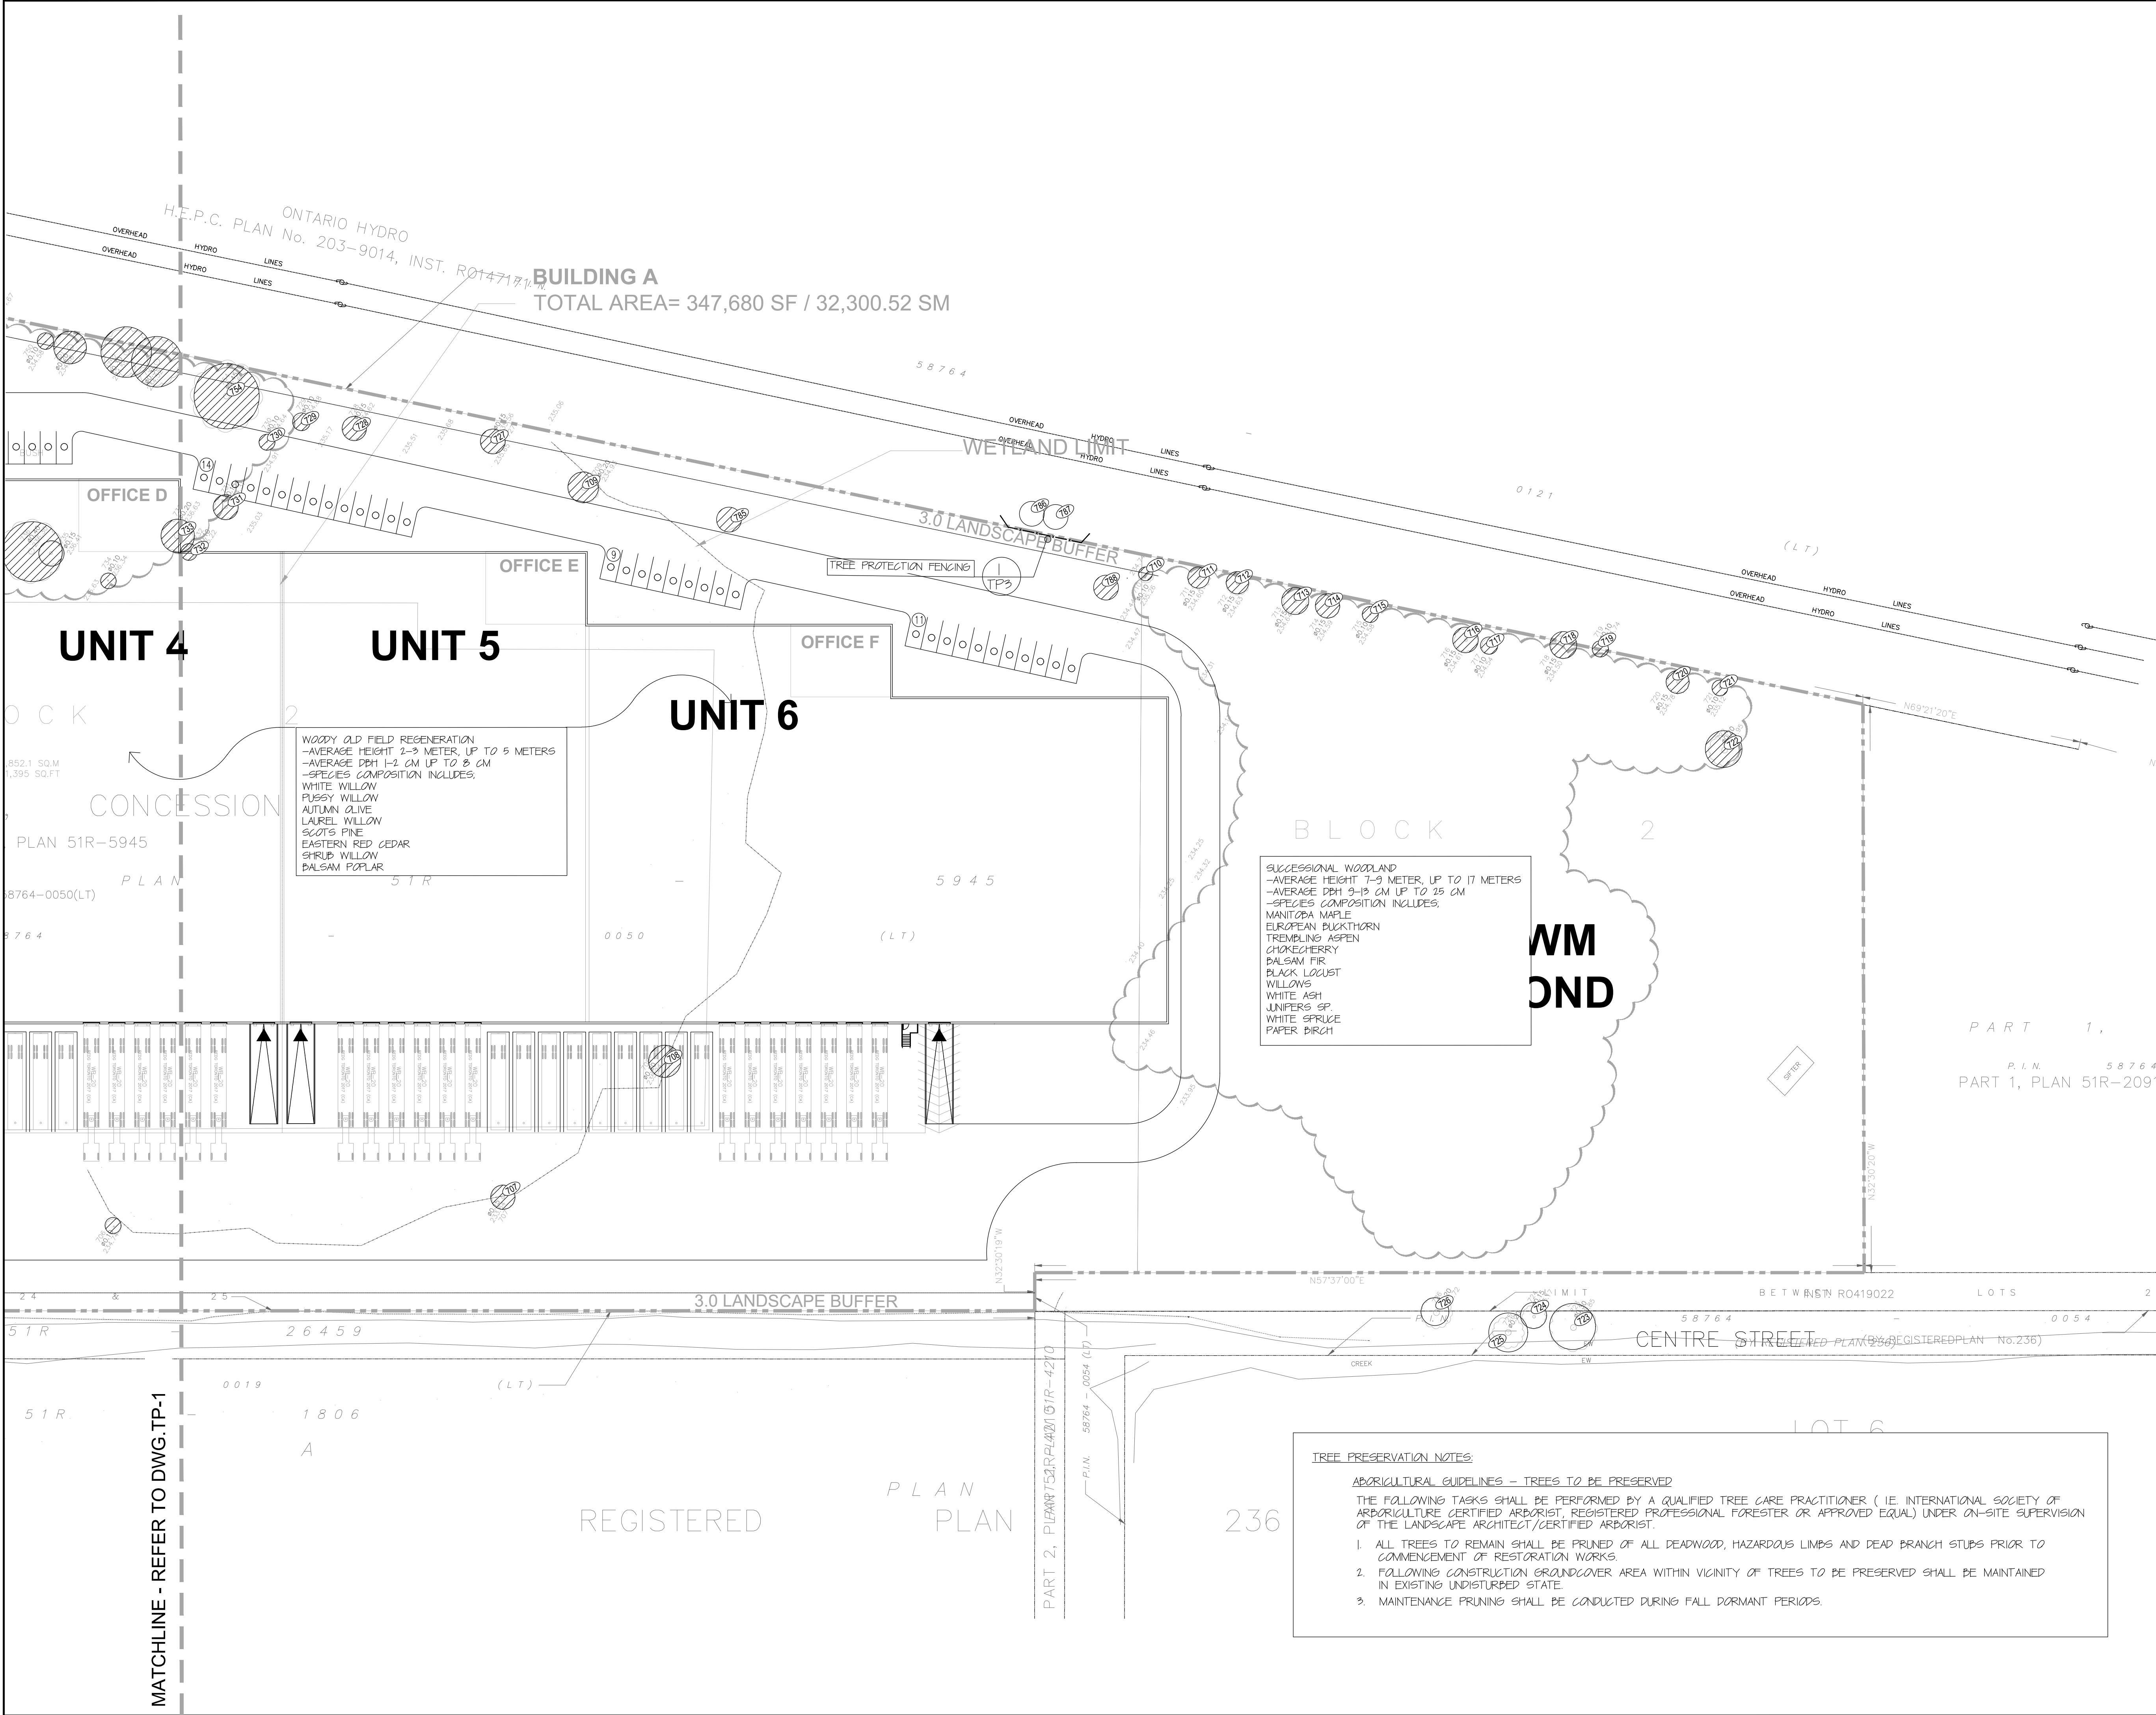

LEGEND	
	PROPERTY LINE
	PROPOSED TREE PRESERVATION FENCING
	TAG NUMBER EXISTING DECIDUOUS TREE TO BE PRESERVED PAGE ELEVATION
	TAG NUMBER EXISTING TREE TO BE REMOVED PAGE ELEVATION

GENERAL NOTES:


- THIS PLAN TO BE USED FOR TREE PRESERVATION AND REMOVAL PURPOSES ONLY.
- BASE INFORMATION OBTAINED FROM KOHN PARTNERSHIP ARCHITECTS Inc., PROJECT NO18-126 AND JDBARNES OLS REFERENCE No19-25-681-00
- FOR TREE PRESERVATION NOTES AND DETAILS REFER TO DWG. TP-2
- FOR TREE INVENTORY LIST REFER TO DWG. TP-3
- CONTRACTOR TO PROVIDE 48 HOURS NOTICE TO LANDSCAPE ARCHITECT PRIOR TO COMMENCEMENT OF WORK

Revisions	
1	ISSUED FOR CLIENT REVIEW
No.	By Date

This drawing is not to be used for construction unless signed by the Landscape Architect.

Approved by:..... Date:.....

All drawings are the property of the consultant and may not be used or reproduced without permission. The contractor shall check and verify all dimensions on site. This drawing must not be scaled.

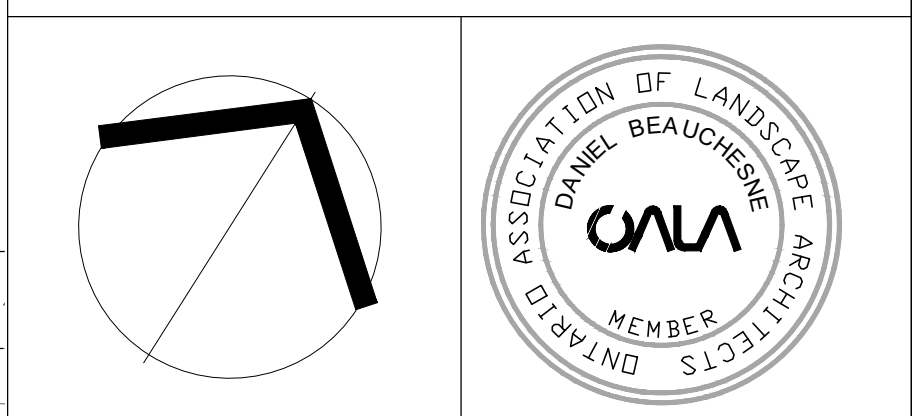

COSBURN GIBERSON LANDSCAPE ARCHITECTS
30 Centurian Drive, Suite 210, Markham, Ontario L3R 8B8
Telephone 905-475-6988 Fax 905-475-5930 info@cgl.ca

Client
**545 DUNLOP STREET
FIRST GULF DEVELOPMENTS
BARRIE, ON
CITY OF BARRIE**

Title
TREE PRESERVATION PLAN

Drawn SS	Scale 1:500	Drwg File 2855-TP
Checked DB	Date Oct. 03, 2022	Drawing No.
Approved DB	Project No. 2855	TP-2

TREE PRESERVATION NOTES

1. THE CONTRACTOR WILL BE CAREFULLY AND THOROUGHLY INFORMED BY THE DEVELOPER OF HIS CONTRACTUAL OBLIGATIONS REGARDING TREE AVOIDANCE AND PRESERVATION, AS WELL AS MAINTENANCE MEASURES TO BE UNDERTAKEN PRIOR TO COMMENCEMENT OF ANY SITE WORK.
2. THE DEVELOPER IS REQUIRED TO BE INFORMED ABOUT THE WILDLIFE ACT AND MIGRATORY BIRD CONVENTION ACT, 1994 (M-701-C.R.C., c.1035 GENERAL PROHIBITIONS, SECTION 6) REQUIREMENTS TO ENSURE CONFORMANCE WITH PROVINCIAL AND FEDERAL REGULATIONS. IT IS AN OFFENCE TO DESTROY ACTIVE NESTS AND/OR EGGS DURING BIRD NESTING PERIODS. COMMON NESTING PERIODS EXTEND FROM APRIL 1ST TO JULY 31ST FOR MOST BIRDS. NESTING CAN OCCUR AT OTHER TIMES AS WELL. LARGE SCALE CLEARING OPERATIONS ARE PROHIBITED DURING THIS PERIOD, UNLESS APPROPRIATE MONITORING IS UNDERTAKEN. SHOULD TREE REMOVAL DURING BIRD NESTING SEASON BE UNAVOIDABLE, THE DEVELOPER IS REQUIRED TO CONDUCT A NESTING SURVEY. IN ADDITION, THE DEVELOPER IS ALSO REQUIRED TO PROVIDE ON-SITE MONITORING BY A REGISTERED PROFESSIONAL BIOLOGIST TO ENSURE NESTS WILL NOT BE DAMAGED.
3. THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST WILL BE RETAINED ON SITE BY THE DEVELOPER WITH A HARD COPY OF THE APPROVED TREE PRESERVATION PLAN DURING CRITICAL STAGES OF GRADING AND CONSTRUCTION TO ENSURE STRICT ADHERENCE TO ITS RECOMMENDATIONS AND TO SUPERVISE THOSE ELEMENTS OF THE PROJECT THAT RELATE TO THE PRESERVATION OF THE TREES.

4. CONTRACTORS ARE RESPONSIBLE TO IMPLEMENT ALL TREE PRESERVATION MEASURES TO THE SATISFACTION OF THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST. WHERE DIRECTED BY THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST, THE CONTRACTOR WILL REPLACE ALL DAMAGED OR DESTROYED EXISTING PLANT MATERIAL AFFECTED DURING THE COURSE OF CONSTRUCTION WITH THE FOLLOWING CONDITIONS AND TO THE SATISFACTION OF THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST AND THE TOWN:
- WITH PLANT MATERIAL OF IDENTICAL OR SIMILAR SPECIES,
 - OF EQUAL OR GREATER SIZE, AND,
 - IN SAME QUANTITY

PROTECTIVE FENCING

- THE CONTRACTOR WILL PROVIDE PROTECTIVE FENCING PRIOR TO COMMENCEMENT OF ANY SITE WORK TO ALL EXISTING INDIVIDUAL TREES AND ASSOCIATED UNDERSTOREY AND GROUNDCOVER, WHICH ARE TO REMAIN. GROUPS OF TREES AND OTHER EXISTING PLANTINGS TO BE PROTECTED WILL BE DONE IN A LIKE MANNER WITH FENCING AROUND THE ENTIRE CLUMPS(S). THE FENCING WILL BE LOCATED 360 DEGREES AROUND SINGLE OR CLUMP(S) OF PROTECTED TREES.
- PROTECTIVE TREE FENCING WILL BE DEFINED AS ORANGE PLASTIC COVERED FARM WIRE FENCING WITH A HEIGHT OF 1200mm.
- THE CONTRACTOR WILL INSTALL PROTECTIVE FENCING ON (50mm X 50mm X 6mm) - 2400mm LENGTH STEEL T-BARS POSITIONED 150mm ON CENTRE MAXIMUM. THE PROTECTIVE FENCING WILL BE WIRED IN THREE (3) PLACES EVENLY SPACED ALONG THE STEEL T-BAR WITH #10 GALVANIZED WIRE.
- THE LANDSCAPE ARCHITECT/ISA ARBORIST WILL INSPECT AND THE CONTRACTOR WILL MAINTAIN PROTECTIVE FENCING REGULARLY IN GOOD REPAIR. PROTECTIVE FENCING SHALL REMAIN IN PLACE THROUGHOUT THE DURATION OF CONSTRUCTION AND SHALL NOT ALLOW TRAFFIC, VEHICLES, FOOT TRAFFIC OR EQUIPMENT TO COMPACT SOIL WITHIN THE TREE PROTECTION ZONES. ACCESS ROUTES SHOULD BE ESTABLISHED AWAY FROM PROTECTED AREAS.
- INSTALLATION OF PROTECTIVE FENCING WILL BE COMPLETED PRIOR TO THE COMMENCEMENT OF SITE CLEARANCE, DEMOLITION OR ANY OTHER TYPE OF CONSTRUCTION TO THE SATISFACTION OF THE ISA CERTIFIED ARBORIST AND THE CITY, AND REMAIN INTACT THROUGH THE COMPLETION OF CONSTRUCTION WORKS. ANY PROTECTIVE FENCING INSTALLED IS THE RESPONSIBILITY OF THE CONTRACTOR. ONCE CONSTRUCTION WORKS HAVE BEEN COMPLETED, CONTRACTOR IS RESPONSIBLE FOR THE COMPLETE REMOVAL OF THE PROTECTIVE FENCING.
- AREAS WITHIN THE PROTECTIVE FENCING WILL REMAIN UNDISTURBED AND WILL NOT BE USED FOR STORAGE OF BUILDING MATERIALS OR EQUIPMENT.

7. WHERE ROOT SYSTEMS OF PROTECTIVE TREES ARE EXPOSED DIRECTLY, ADJACENT TO OR ARE DAMAGED BY CONSTRUCTION WORK, THEY WILL BE TRIMMED NEATLY AND THE AREA BACKFILLED WITH APPROPRIATE MATERIAL TO PREVENT DESICCATION.
8. SHOULD THE ROOT SYSTEM OR ABOVE GROUND COMPONENTS, OF ANY TREES DESIGNATED TO REMAIN SUSTAIN MINOR DAMAGE, AS DETERMINED BY AN ISA CERTIFIED ARBORIST, REMEDIATION OF THE DAMAGE WILL BE THE RESPONSIBILITY OF THE CONTRACTOR AND AT THE ADVICE OF THE ISA CERTIFIED ARBORIST. IF IRREPARABLE DAMAGE HAS OCCURRED, THE TREE BECOMES UNSAFE OR LIABILITY IS QUESTIONABLE, THE CONTRACTOR WILL BE REQUIRED TO REMOVE THE TREE(S) AND RE-ESTABLISH THE TREE(S) TO THE SATISFACTION OF THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST AND THE CITY.
9. IN THE EVENT THAT IT IS ESSENTIAL FOR LARGE (70M TO 80M DIAMETER) ROOTS TO BE CUT, EXCAVATED OR INJURED DURING CONSTRUCTION, THE ROOTS WILL BE CUT FLUSH UNDER THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST'S SUPERVISION AND IN ACCORDANCE WITH APPROVED ARBORICULTURAL PRACTICES.

PROTECTIVE MEASURES

10. PRUNING PRACTICES
- SANITATION, PRUNING, ROOT FEEDING, WATERING DURING DRY SEASON, AD OTHER TREE PROTECTIVE MEASURES SHOULD BE CARRIED OUT DURING CONSTRUCTION OF OPTIMUM RESULTS, AS FOLLOWS:
- PRUNING PRACTICES
- ALL LIMBS DAMAGED OR BROKEN DURING THE COURSE OF CONSTRUCTION WILL BE PRUNED CLEANLY, UTILIZING CLEAN, SCISSOR ACTION (NOT ANVL TYPE) SECATEURS IN ACCORDANCE WITH APPROVED ARBORICULTURAL PRACTICES.
 - ROOTS OF EXISTING TREES THAT ARE DISTURBED BY EXCAVATION OR ANY OTHER CONSTRUCTION ACTIVITY WILL BE CLEANLY PRUNED, AS DIRECTED BY THE ISA CERTIFIED ARBORIST. TOOLS MUST BE DISINFECTED AFTER PRUNING A TREE AND WHEN PRUNING ANY MEMBERS OF THE SAME GENERAL, TO PREVENT THE SPREAD OF DISEASE.
 - ALL PRUNING CUTS WILL BE MADE TO A GROWING POINT SUCH AS A BUD, TWIG OR BRANCH. NO STUBS SHOULD BE LEFT. POOR CUT LOCATION, POOR CUT ANGLE AND TORN CUTS ARE NOT ACCEPTABLE. PRUNING OF THOSE TREES, WHERE HEAVY BLEEDING MAY OCCUR, IS TO BE POSTPONED UNTIL IN FULL LEAF. DO NOT DAMAGE LEAD BRANCHES OR REMOVE SMALLER TWIGS ALONG MAIN BRANCHES.
- PRUNING SHOULD INCLUDE THE CAREFUL REMOVAL OF:
- DEADWOOD
 - BRANCHES THAT ARE WEAK, DAMAGED, OR DISEASED
 - SECONDARY LEADERS OF CONIFERS
 - TRUNK AND ROOT SUCKERS
 - TRUNK WATERSPOUTS
 - TIGHT V-SHAPED OR WEAK CROTCHES
 - BRANCHES THAT RUB CAUSING DAMAGE TO BARK
- THE CONTRACTOR, ON DIRECTION FROM THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST, WILL BE REQUIRED TO WATER LARGE TREES A MINIMUM OF THREE (3) TIMES DURING THE SUMMER OR AS REQUIRED.

EXCAVATING AROUND EXISTING TREES

THIS PROCEDURE IS TO BE UNDERTAKEN ONLY AT THE DIRECTION, SUPERVISION AND APPROVAL OF THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST AND IN REFERENCE TO THE FOLLOWING CHART- TABLE 1: TREE PROTECTION ZONES FOR INDIVIDUAL SPECIMEN TREES, SHOWING MINIMUM DISTANCES REQUIRED FOR DETERMINING A TREE PROTECTION ZONE. SOME TREES AND SOME SITE CONDITIONS MAY REQUIRE A LARGER TREE PROTECTION ZONE.

TABLE 1: TREE PROTECTION ZONES FOR INDIVIDUAL SPECIMEN TREES

TRUNK DIAMETER (cm)	MINIMUM PROTECTION DISTANCE REQUIRED BEYOND DRIPLINE (m)
(MEASUREMENT OF A TREE TRUNK TAKEN AT 14m ABOVE GRADE)	(TREE PROTECTION ZONE DISTANCE MEASURED FROM OUTSIDE EDGE OF DRIPLINE)
LESS THAN 10	1.5
11-40	2.4
41-50	3.0
51-60	3.6
61-70	4.2
71-80	4.8
81-90	5.4
91-100	6.0

- THE DEVELOPER/OWNER MAY BE REQUIRED TO UNDERTAKE PRESERVATION TECHNIQUES SUCH AS DRY WELLING AND ROOT FEEDING.
- ALL FILLING AND GRADING THAT IS APPROVED WITHIN A TREE RETENTION AREA WILL BE COMPLETED BY HAND.
- EXCAVATION TO BE PERFORMED ON ONLY ONE SIDE OF THE TREE. ALL OTHER GRADE CHANGES WILL BE MADE OUTSIDE OF THE DRIP LINE. CUT SLOPE FROM MINIMUM PROTECTION DISTANCE TO DRIPLINE REQUIRED IN TABLE 1: TREE PROTECTION ZONES FOR INDIVIDUAL SPECIMEN TREES TO NEW GRADE LEVEL. BUILD A TOPSOIL DYKE AROUND DRIPLINES TO RETAIN WATER AS REQUIRED.
- IF EXCAVATION THROUGH ROOTS IS REQUIRED, EXCAVATE BY HAND AND PRUNE ROOTS WITH A SHARP AXE, TREE LOOPER OR SAW. CONDUCT ROOT PRUNING ACCORDING TO AFOREMENTIONED GUIDELINES ON PRUNING.
- THE AREAS SURROUNDING THE ROOT SYSTEM SHALL BE BACKFILLED IMMEDIATELY WITH NATIVE MATERIAL AFTER DAMAGE OCCURS TO PREVENT DRYING AND/OR DIE-BACK.


12. CLEARING OPERATIONS SHOULD BE IDENTIFIED IN AREAS INCLUDING BUILDING SITINGS, PARKING LOTS, RIGHT OF WAYS AND CUT/FILL EARTHWORK ZONES. ANY TREES LOCATED DOWNHILL OF WATER FLOW WILL BE PROTECTED FROM SILTATION BY STRAW DALES AND/OR SILTATION FENCE.
13. AFTER CONSTRUCTION, ALL PRESERVATION VEGETATION SHOULD BE INSPECTED FOR ITS STATE OF HEALTH BY THE ISA CERTIFIED ARBORIST AND THE CITY OF BARRIE.

GENERAL TREE PRESERVATION AND PROTECTION NOTES


14. THE AREA WITHIN DRIPLINE OF ALL EXISTING TREES AND/OR AREAS TO BE PROTECTED WILL BE PROPERLY PROTECTED WITH FENCING AS DETAILED. ALL EXISTING TREES, WHICH ARE TO REMAIN ON SITE, OR ON ADJACENT PROPERTIES WHICH MAY BE AFFECTED, WILL BE FULLY PROTECTED WITH PROTECTIVE FENCING ERECTED 1.0m OUTSIDE THE "DRIP LINE" OF TREES, OR IN THE CASE OF INDIVIDUAL SPECIMEN TREES, AS PER TABLE 1: TREE PROTECTION ZONES FOR INDIVIDUAL SPECIMEN TREES, PRIOR TO COMMENCEMENT OF CONSTRUCTION.
15. AREAS WITHIN THE PROTECTIVE FENCING WILL REMAIN UNDISTURBED, AND WILL NOT BE USED FOR THE STORAGE OF BUILDING MATERIALS, EQUIPMENT, SURPLUS SOIL, OR CONSTRUCTION DEBRIS. THIS WILL BE COMPLETED PRIOR TO THE COMMENCEMENT OF SITE CLEARANCE, DEMOLITION, OR ANY OTHER TYPE OF CONSTRUCTION WORKS TO THE SATISFACTION OF THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST, AND THE CITY OF BARRIE.
16. NO CONSTRUCTION ACTIVITY, GRADE CHANGES, SURFACE TREATMENT OR EXCAVATIONS OF ANY KIND ARE PERMITTED WITHIN THE TREE PROTECTION ZONE.
17. NO RIGGING CABLES SHALL BE WRAPPED AROUND OR INSTALLED IN TREES AND/OR PROTECTED AREAS.
18. NO CONTAMINANTS SHALL BE DUMPED OR FLUSHED WHERE FEEDER ROOTS OF PROTECTED TREES AND/OR AREAS EXIST.
19. THE DEVELOPER AND/OR CONTRACTOR WILL TAKE EVERY PRECAUTION NECESSARY TO PREVENT DAMAGE TO TREES, SHRUBS OR OTHER PLANTS TO BE RETAINED.
20. WHERE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST APPROVES, LIMBS OR PORTIONS OF TREES ARE TO BE REMOVED TO ACCOMMODATE CONSTRUCTION WORK, THEY SHALL BE REMOVED CAREFULLY IN ACCORDANCE WITH ACCEPTED ARBORICULTURAL PRACTICE AND MEASURES WILL BE TAKEN TO PREVENT ANY FURTHER DAMAGE.
21. IF GRADES AROUND THE TREES TO BE PROTECTED ARE LIKELY TO CHANGE, PRECAUTIONS MUST BE UNDERTAKEN TO THE SATISFACTION OF THE ISA CERTIFIED ARBORIST AND THE CITY. THESE PRECAUTIONS ARE THE RESPONSIBILITY OF THE DEVELOPER AND/OR THE CONTRACTOR. THESE PRECAUTIONS MAY INCLUDE DRY WELLING AND ROOT FEEDING, AND MUST BE IN ACCORDANCE WITH THE AFOREMENTIONED TREE PRESERVATION GUIDELINES.
22. TREES THAT HAVE DIED OR BEEN DAMAGED BEYOND REPAIR WILL BE REPLACED BY THE CONTRACTOR AT HIS OWN EXPENSE BY TREES OF A SIMILAR SIZE AND SPECIES OR SUCH SIZE AND SPECIES AS MAY BE APPROVED BY THE ISA CERTIFIED ARBORIST AND THE CITY OF BARRIE.
23. ANY TREES DESIGNATED FOR REMOVAL SHALL HAVE THE STUMPS COMPLETELY EXCAVATED AND REMOVED UNLESS SUCH REMOVAL WILL ADVERSELY AFFECT EXISTING TREES/ECOLOGY TO REMAIN, IN WHICH CASE TRUNKS WILL BE CUT TO EXISTING GRADES.
24. ALL WOODY MATERIAL REMOVED WILL BE RECYCLED AS DIRECTED BY THE CITY OF BARRIE, AND USED FOR FENCE POSTS, SAW LOGS, FIREWOOD OR WOODCHIPS WHERE APPROPRIATE.

SITE INSPECTIONS


25. PRIOR TO ANY REMOVAL OF THE TREES AND/OR PLANT MATERIAL, INSTALLATION PROTECTIVE BARRIERS AND ANY SITE GRADING, A CONSTRUCTION MANAGEMENT MEETING WILL BE HELD ON THE SITE REPRESENTATIVES FROM THE CITY OF BARRIE PLANNING DEPARTMENT, THE LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST, AND THE GENERAL CONTRACTOR.
- DURING THE MEETING/INSPECTION:
- TREES TO BE REMOVED WILL BE FLAGGED INCLUDING THOSE TREES AND LIMB WITH HIGH RISK OF FAILURE.
 - PROTECTIVE FENCING WILL BE STAKED OUT WHERE REQUIRED; AND,
 - AGREEMENT WILL BE MADE ON WHEN AND HOW THE WORKS BEGIN, AND WHEN THE WORKS WILL BE COMPLETED.
26. ALL TREE PRESERVATION ZONES WILL BE INSPECTED BY THE REQUIRED REPRESENTATIVES FROM THE CITY OF BARRIE (PLANNING DEPARTMENT), LANDSCAPE ARCHITECT/ISA CERTIFIED ARBORIST AND THE DEVELOPER/OWNER AND/OR CONTRACTOR FOLLOWING INSTALLATION OF PROTECTIVE BARRIERS AND REMOVAL OF ALL DEAD OR DECLINING MATERIAL.

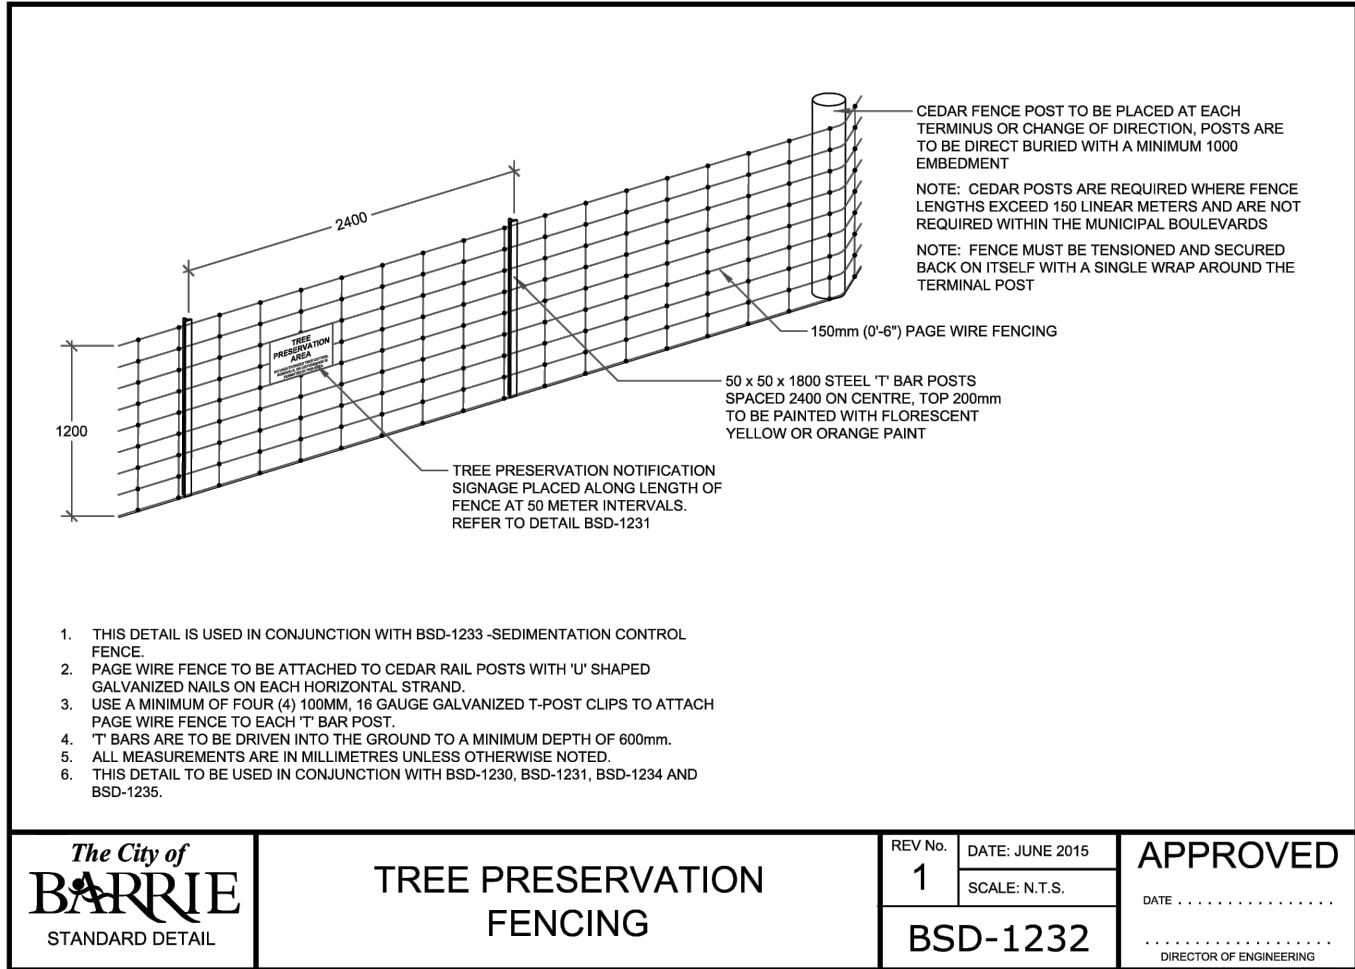

1 TREE PROTECTION FENCING

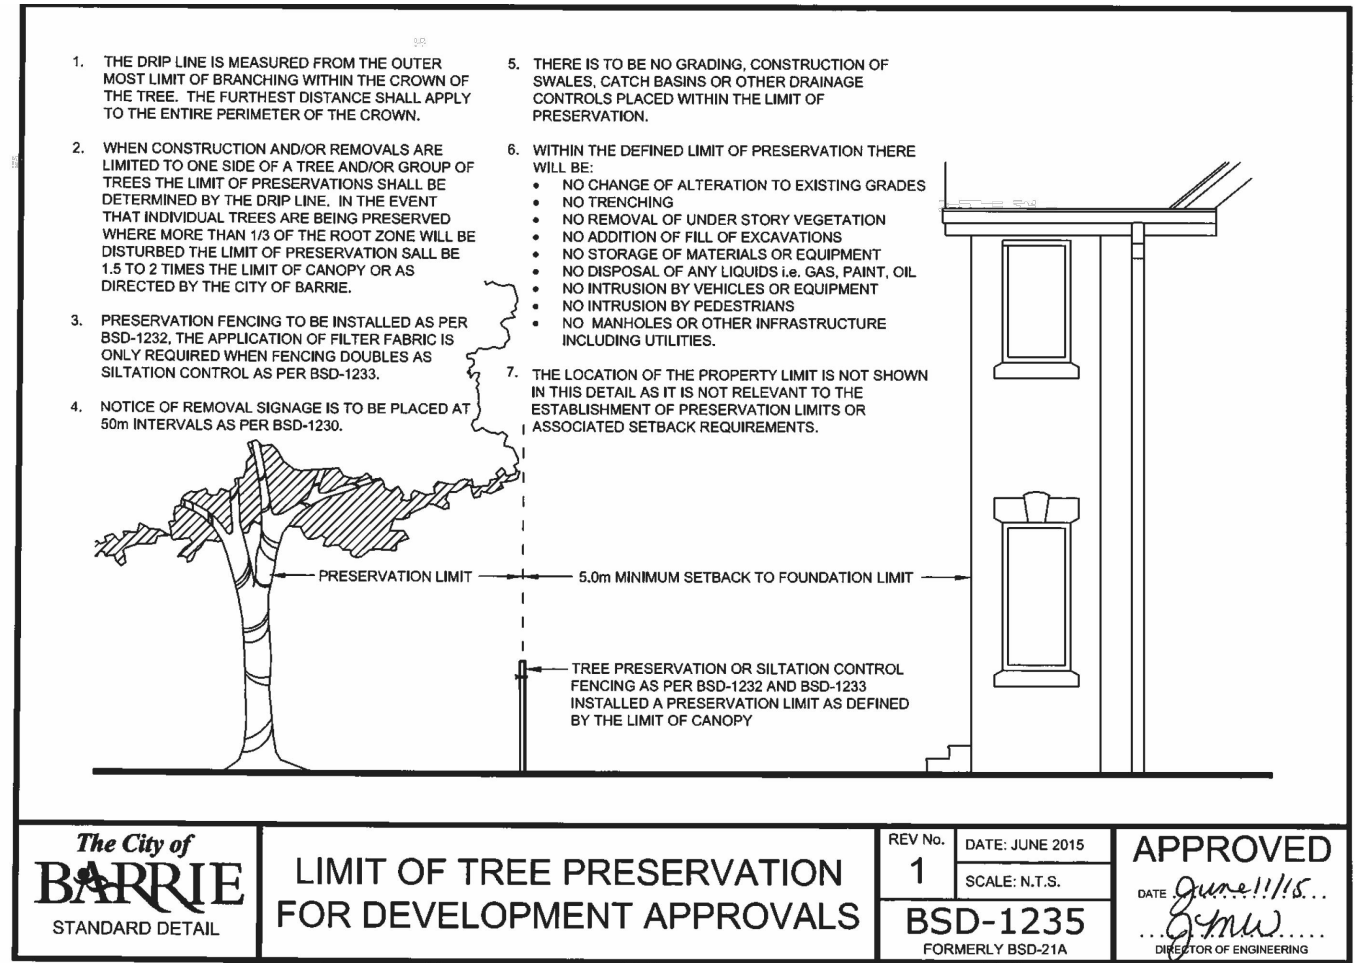

2 LIMIT OF TREE PRESERVATION FOR DEVELOPMENT APPROVAL

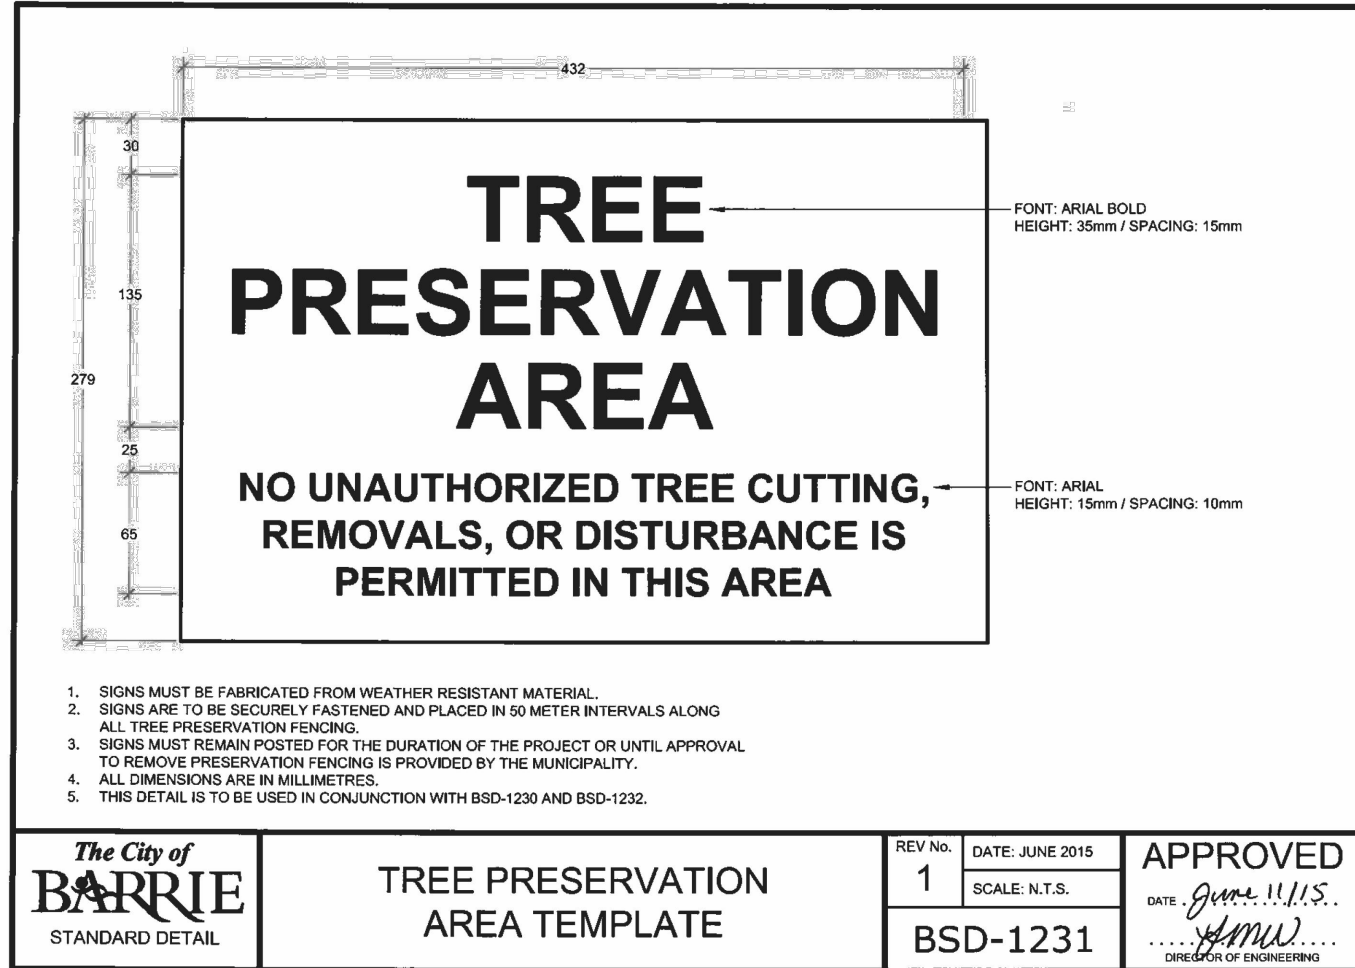

3 TREE PRESERVATION AREA TEMPLATE

1	ISSUED FOR CLIENT REVIEW	SS	DEC. 19/20
No.		By	Date
Revisions			
This drawing is not to be used for construction unless signed by the Landscape Architect.			
Approved by:.....		Date:.....	
All drawings are the property of the consultant and may not be used or reproduced without permission. The contractor shall check and verify all dimensions on site. This drawing must not be scaled.			
		30 Centurian Drive, Suite 210, Markham, Ontario L3R 8B8 Telephone 905-475-6988 Fax 905-475-5930 info@cgl.ca	
Client 545 DUNLOP STREET FIRST GULF DEVELOPMENTS BARRIE, ON CITY OF BARRIE			
Title TREE PRESERVATION NOTES AND DETAILS			
Drawn	Scale	Drwg File	
SS	1:500	2855-TP	
Checked	Date	Drawing No.	
DB	OCT. 03, 2022		
Approved	Project No.		
DB	2855		

TP-3
